M. A. R. 57 (Rule 116) No. E 559602

Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency..... H: Gangadhar .....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work : Providing pathway & other development works to Ganesha Layout park in M.S Palya ward no 11						
	Est cost : 19.90 lakhs						
	Job code No : 011-15-000099 22						
	Head of account : P0190						
	Work order No : BBMP/EE/BTP/WO/245/16-17						dt : 25/03/17
	D.O.R : 26/8/21						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	(c) Earthwork en surface excavation & ordinary soil for levelling & lowering the ground manually & removing the excavated stuff to a distance not exceeding 50mt & lift upto 1.5m excavated surface levelled & neatly dressed, disposed earth to be reused after breaking of clods & neatly dressed.						
	Prem measurement recorded at vide I.NO (1) of P.4 NO 559668 of this M.B					1220.68	176999.00
	exp 145/-						
	(d) Earth work excavation for foundation of building water supply sanitary line & electrical condition either in pits or in trenches 1.5m & above in hard soil not exceeding 1.5 mt in depth including						

M. A. R. 57 (Rule 116) No. E 559603
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	dressing the bottom & sides of pits trenches, shoring the excavated soil clear from edges of excavation with lead upto 50 M after breaking						
	Prem measurement recorded at vide I.NO (2) of P4 NO 559669 of this M.B					84.74	220320.00
	exp 260/-						
	(d) lead for disposal of dubris/earth shall be payable at garage rate by mechanical means including loading & unloading from 1/4 km to 15 kms						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Premeasurement recorded at vide 1.NO (3) of P.H NO 559669 of this M.B					1097.0	136185.00
					ERE 105/-		
(4)	Providing & fixing precast solid concrete kerb stone made out of CC 1:2:4 & finished with Cm 1:3 plastering & finishing cutting etc						
	North side	2	30.0	-	-	60.0	
		2	30.0	-	-	60.0	
		2	7.0	-	-	14.0	
	North middle side	2	30	-	-	60.0	
		2	2.7	-	-	5.4	
	South side	2	19.0	-	-	38.0	
		2	30.0	-	-	60.0	
		2	9.5	-	-	19.0	
		2	24.0	-	-	48.0	
						364.4	

M. A. R. 57 (Rule 116) No. E 559604
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	East side	2	30.0	-	-	60.0	364.4
	East middle side	2	25.0	-	-	50.0	
		2	13.5	-	-	27.0	
		2	30.0	-	-	60.0	
	West side	2	17.0	-	-	34.0	
		2	30	-	-	60.0	
		2	30	-	-	60.0	
	Around Gazibo	2	15.5	-	-	31.0	
		2	30	-	-	60.0	
		2	5.0	-	-	10.0	
						816.40	
						0.45	
				816.40	0.45	1814	607950.00
					limited to	1737	
					Cr 350/-		

Cafe Mehfuz 2nd

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
(5)	Providing & laying heavy duty cobble stone 60mm thick interlocke pavers upto Cement & Coarse sand for manufacture of blocks of approved size shape & colour with a minimum Compressive strength of 28 kgs/sq.mm upto 50mm thick sand bed & compacting with plate Vib rator having 2 tons Compaction force thereby forcing dust of sand under mesh to come up in between joints final compaction of pavers surface joints on to it final level including cost of material, labour & item of machinery Complete						
	North side	1	30.0	3.0	-	90.0	
		1	30.0	3.0	-	90.0	
		1	7.0	3.0	-	21.0	
	North middle line	1	30	3	-	90.0	
						291.0	

M. A. R. 57 (Rule 116) No. E

Measurement Book

559605

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		1	27	3.0	-	8.1	291.0
	South side	1	19	3.0	-	57.0	
		1	30	3.0	-	90.0	
		1	9.5	3.0	-	28.5	
		1	24.0	3.0	-	72.0	
	East side	1	30.0	3.0	-	90.0	
		1	25.0	3.0	-	75.0	
		1	13.5	3.0	-	40.5	
	east middle side	1	30.0	3.0	-	90.0	
		1	17.0	3.0	-	51.0	
	west side	1	30.0	3.0	-	90.0	
		1	30.0	3.0	-	90.0	
						1073.1	

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		1	155	3.0	-	46.50	1073.1
	Around the Gazibo	1	30.0	3.0	-	90.0	
		1	5.0	2.0	-	15.0	
						1224.60	
						Limited to 1088.90	95708400
						Cft 883/-	
6	Providing & fabricating, supplying & erecting to plumb & line MS grill work as per approved design & drawing using 50x50x6mm angle of heavy guage as support & 25x25x6mm angles of heavy guage for frame work with 100x50mm channel section to join grills 16mm & 10mm square rod are used for vertical at 75mm c/c alternately 25x25x6mm equal angel to be provided horizontally one at top & at bottom. The work is inclusive of thoughning angle square rod & angles square rod channel welding to suitable						

M. A. R. 57 (Rule 116)

Measurement Book

No. E 559606

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency. .....

Date of commencement of work. .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Size for each bay, all the joints are welded together including grinding, finishing metal parts & painting a coat of anti corrosive paint over one coat of primer. the rate is inclusive of all material like MS angles, hold fast, cost of labour for all items of work cost of painting welding cutting lathe work grinding thoughning including loading & unloading with all lead & lift charges	1	3.0	-	2.0	6.0	27240.00
						Cft 4540/-	
1	Providing & applying ready mix foaming coat over concrete masonry / asbestos cement sheet plastered surface including						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Preparing the surface after through brooming cost of materials labour						
	N/side	2	30.0	–	0.35	21.0	
		2	30.0	–	0.35	21.0	
		2	7.0	–	0.35	4.9	
	N/middle line	2	30.0	–	0.35	21.0	
		2	2.7	–	0.35	1.89	
		2	19.0	–	0.35	13.30	
	S/side	2	30.0	–	0.35	21.0	
		2	9.5	–	0.35	6.65	
		2	24	–	0.35	16.80	
	East/side	2	30	–	0.35	21.0	
		2	25	–	0.35	17.50	
	east middle s/d	2	13.5	–	0.35	9.45	
						175.49	

M. A. R. 57 (Rule 116) No. E 559607

Measurement Book

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		2	30	–	0.35	21.0	175.49
		2	17	–	0.35	11.9	
		2	30	–	0.35	21.0	
		2	30	–	0.35	21.0	
		2	15.5	–	0.35	10.85	
		2	30.0	–	0.35	21.0	
	Around gaji bo	2	5.0	–	0.35	3.5	
						285.54	
				Waisted k		273.58	6290.00
				cm 02			

16/8

16/8/11

Assistant Executive Engineer
Vijayanagara Sub Division
BDMP, Bangalore-97

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
(8)	providing & applying painting with ready mix paint in two coats over new concrete/asbestos cement sheet plastered surface brush to give an even shade after preparing the surface after thrugh brooming of oil dirt & other foreign matter & good papering including cost of material labour						
	Qty same as vide item No (8)					273.58	12311.00
	@ 45/-						
(9)	providing & fixing chujja bon as per design drawing						
		2	-	-	2		9560.00
				@ 4780/-		Total =	1955653.00

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

M. A. R. 57 (Rule 116) No. E 559608
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Certificate						
1)	Contractor carried it own men & material						
2)	There is no due from contractor to BBMP Pertaining to the work						
3)	work done satisfactorily						

2018

Assistant Executive Engineer
Vidyaranyapura Sub Division
BBMP, Bangalore - 97

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Ganesha layout
park

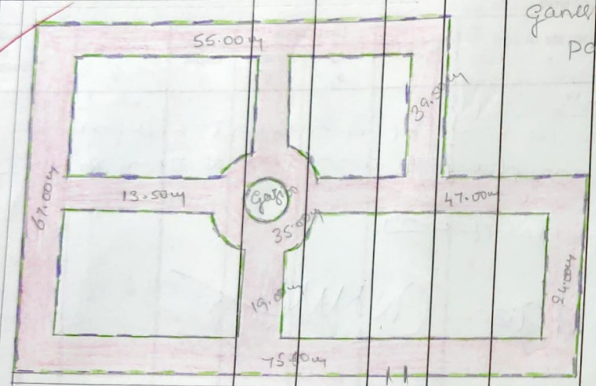

Assistant Executive Engineer
Yelahanka Sub Division

M. A. R. 57 (Rule 116)
Measurement Book

No. E 559609

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

First & Final

ಲೆಕ್ಕಶೀರ್ಷಿಕೆ P-0190 ರಡಿ
ಬಿಲ್ಲು ಮೊಬಲಗು ರೂ. 1955600=00 ಗಳನ್ನು ಪಾಸು ಮಾಡಿದೆ.
ಇದರಲ್ಲಿ ರೂ. 99490=00 ಗಳನ್ನು ಹೊಂದಾಣಿಕೆ
ಮಾಡಿಕೊಂದು ರೂ. 1856110=00 ಗಳನ್ನು
1406310=00
FT/NEFT/RTGS ಮುಖಾಂತರ ನೀಡಲಾಗಿದೆ

ಸಹಾಯಕ ಲೆಕ್ಕಾಧಿಕಾರಿ / ಲೆಕ್ಕಾಧಿಕಾರಿ / ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಬಿಬಿಎಂಪಿ ಬ್ಯಾಟರಾಯನಪುರ ವಿಭಾಗ ಬ್ಯಾಟರಾಯನಪುರ ವಿಭಾಗ
ಬೃಹತ್ ಬೆಂ.ಪಾ. ಬೆಂಗಳೂರು ಬೃಹತ್ ಬೆಂ.ಪಾ. ಬೆಂಗಳೂರು

	BA -	1955600=00
2T	-	19566=00
LC	-	19566=00
CGC	-	1956=00
CGST	-	17461=00
SGST	-	17461=00
LR	-	7000=00
EOT	-	16600=00
TD	-	99490=00
	Cost -	1856110=00
	(-) TDS -	449800=00
	Total =	1406310=00

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರ
